

CITIZENS' BOND OVERSIGHT COMMITTEE

2006 BOND UPDATE PRESENTATION MEASURE R

Rowland Unified School District

May 28, 2014



Program Update: AGENDA

A. Program Update


B. Financial Report

c. Project Expenditure Report



A. Program UpdateScope

Rowland High School

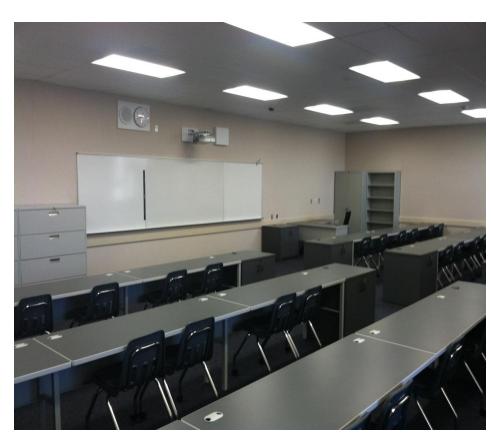

New CTE Business Classroom Smart Board, & Office Environment Furniture



Modernized Building Exterior New Lockers, ADA Compliant Flatwork, Stucco, Paint, New Doors & Hardware



A. Program Update Scope (Cont.)

Rowland High School





New Classroom
Data Raceway, Projector, & Improved Interior
Finishes

New Classroom
Casework, VCT Flooring & Whiteboard



A. Program Update Scope (Cont.)

Nogales High School Revival



New Building "B" Structural Steel Erection As of 5/22/14



New Building "C" Slab Forms, Utilities & Rebar As of 5/22/14



A. Program Update Scope (Cont.)

Nogales High School Revival



New Building "A" Gas, Sewer, & Fire Service Utilities

New Building "B" Slab & Steel Erection As of 5/22/14



A. Program UpdateSchedule

Projects (since Summer 2009)

| PHASE 1 (2009) | PHASE 2 (2010) | PHASE 3 (2011) | PHASE 4 (2012) | | | PHASE 5 | PHASE 6 (2013- 14) | PHASE 7 (2014-15) |
|--------------------|------------------------|-------------------|-------------------|---|------|--------------|-----------------------------------|----------------------|
| | | | Winter/Spring | Summer | Fall | (2013) | (2013 14) | (2014 13) |
| NHS - Autoshop | Blandford ES | Telesis - Phase 1 | Yorbita ES* | Rowland HS | | | ES Kindergarten Modernizations | |
| NHS - Utilities | RHS - Culinary | Villacorta ES* | Killian ES** | Rorimer ES* | | Rowland ES** | NHS Revival | |
| Ybarra Academy | Hurley ES | Northam ES* | Telesis - Phase 2 | Shelyn ES** | | | | Santana HS |
| | Giano IS | Jellick ES** | | Hollingworth ES | | | | La Seda ES |
| | Jellick - Portables | Alvarado IS | | Giano IS Asphalt/Concrete Repair | | | | |
| | NHS - Portables | Oswalt Academy | | "Beautification" Projects (e.g. Exterior Paint) "Legacy" Projects (e.g. Mechanical ductwork replacement) | | | | |
| | | Nogales HS | | | | | | |

Notes:

1. Bold = Under Construction

2. Bold Italics = Completed

3. [School Name]* = Relocate to La Seda ES during construction
 4. [School Name]** = Relocate to Farjardo ES during construction

5. Nogales HS = Multiple Projects (Modernization, Library, CTE: Business)

6. Rowland HS = Multiple Projects (Modernization, CTE: Business)

7. Santana HS use in review



A. Program UpdateProject Status Report – 4/30/2014

| Project Name | Status | Bids Due | Award Date | Construction Dates | Committed/ Est. Cost at Completion* | | |
|------------------------------------|------------|----------|------------|-----------------------|-------------------------------------|--|--|
| Rowland High School / CTE Business | | | | | | | |
| Partial Modernization | Punch List | | 6/12/2012 | 6/2012 -5/2014 | \$8,610,800/ \$8,805,812 | | |
| Rowland ES | | | | | | | |
| Partial Modernization | Complete | | 12/4/2012 | 12/2012 – 7/2013 | \$3,114,963 | | |
| Nogales HS Revival and Box Culvert | | | | | | | |
| Partial Modernization | 15% | | 11/12/2013 | 11/2013 – 12/2015 | \$25,192,865/ \$11,384,000 *** | | |
| Kindergarten Projects | | | | | | | |
| Multiple Sites (12) | DSA Review | Phased | | 4/2014 – 4/2015 | \$6,500,000** | | |

Notes:

- 1. * = Main Contractor Construction Commitments / Commitments with Pending Change Orders
- 2. ** = Construction Cost Estimate
- 3. *** = 2006 Measure R Bond Allocation; remaining funds from 2012 Measure R Bond.
- 4. Bold Italics = Project Complete No Significant Additional Costs Anticipated



B. Financial ReportBudget

Project Funding Sources

| Sources | Amount |
|---------------------------------------|------------------|
| Measure R 2006 Bond | \$ 117,980,000 |
| Interest Funds | \$ 6,428,352* |
| Revenue Sources – Partial State Funds | \$ 21,921,911 |
| Other District Sources | \$ 2,359,493 |
| Federal Stimulus Funds | Included in Bond |
| Total Revenue: | \$ 148,545,463 |

Note:

* = As of 3/31/2014



C. Fiscal Services Financial Summary:

For the Period Ended April 30th 2014

BEGINNING FUND BALANCE: JULY 1, 2013

REVENUE

Interest – July 2013 to April 30th, 2014

\$ 49,944,115

152,248

LESS: EXPENDITURES PAID (Total All)

July 1, 2013 to April 30th, 2014

\$ 11,188,636

FUND BALANCE AS OF April 30th 2014 MEASURE R 2006

\$ 38,907,727



C. Fiscal Services Financial Summary:

(cont.)

| | Expenditures paid - July 2013 to April 2014 | 2013-14 | 2012-13 |
|-------|--|------------|------------|
| 90300 | Stadium - Nogales, Rowland HS | 0 | 0 |
| 90301 | Library Modernization | 0 | 52,102 |
| 90302 | Playground - La Seda Elementary | 0 | 0 |
| 90303 | Cover Walkway - Rowland Elementary | 0 | 0 |
| 90304 | Multi-Purpose/Kitchen - Villacorta Elementary | 0 | 3,642 |
| 90305 | Library Renovation - Nogales High School | 1,738 | 1,814,053 |
| 90307 | Curb Appeal/Fencing | 0 | 0 |
| 90308 | K-8 Conversion - Ybarra/Oswalt E. Schools/Rincon | 0 | 28,452 |
| 90309 | Career Tech - Nogales/Rowland High Schools: Auto/Cul. | 0 | 2,600 |
| 90310 | New Construction - Oswalt Academy | 20,103 | 3,275,095 |
| 90312 | Kindergarten Mod | 9,436 | 217,707 |
| 90313 | NHS Revival Mod | 4,788,578 | 538,595 |
| 90319 | Career Tech - Nogales/Rowland High Schools: Business | 655,921 | 0 |
| 90400 | Modernization | 5,321,810 | 17,351,631 |
| 90200 | Program Management | 391,050 | 521,400 |
| | TOTALS | 11,188,636 | 23,805,277 |
| | Fund 35.0 (State Matching Funds – C.T.E.) &(Modernization) | 422,913 | 9,682,567 |
| | Trailers Paid by Fund 25.0 (Developer Fees) | 0 | 87,114 |




CBOC Program Update

Questions?



Citizens' Bond Oversight Committee Measure R 2006 – 5/28/2014



THANK YOU





